## Hinchliffe Farm – Progress Newsletter

### Week Ending : 5<sup>th</sup> July 2019

an i o i a i a bait àny agus anna a sur ling ar ann an àrtainn ann ann ann ann ann ann ann ann an àrtainn ann a

#### Key statistics:





A further few weeks into the 'big build' and here's a brief insight into what we have been up to...

- ✓ The first concrete pour to the ground floor has been completed
- ✓ Core driller commenced on site to grind out parts for the mechanical and electrical
- Steel mesh installed ready for the remaining concrete slab to be poured
- Cedar cladding completed
- Plasterers have started skimming walls
- Farmscape cladding completed



Proud to be part of Sewell Group







Back elevation with door installed and fridge carcassing to the left ...



✓ @iandgltdwww.iandgltd.co.uk

Proud to be part of Sewell Group



\*





Remaining slab ready to be installed with the steel mesh in place....



@iandgltd www.iandgltd.co.uk

Proud to be part of Sewell Group



\*





#### First stage of the plastering completed...



✓ @iandgltdwww.iandgltd.co.uk

Proud to be part of Sewell Group







#### Internal aco drain progressing well...



✓ @iandgltd www.iandgltd.co.uk

Proud to be part of Sewell Group



\*





One elevation of the farm scape cladding...




✓ @iandgltd www.iandgltd.co.uk

Proud to be part of Sewell Group



\*



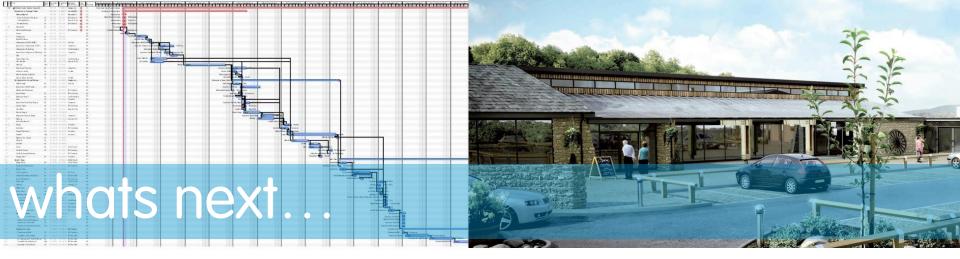

over the next couple of weeks...

- ✓ Fascia's and soffit's to continue
- Remaining slab to be installed did you know an element of the concrete has come from France?
- ✓ Ground worker to continue with external drainage runs
- ✓ M&E throughout
- ✓ Slate roofing to commence once the fascia's and soffit's have been completed
- Remaining internal partitions




Proud to be part of Sewell Group





# building a greener future.





✓ @iandgltd www.iandgltd.co.uk

Proud to be part of Sewell Group



